



## Space Planning & Capital Projects

Backfill Construction Update June 15, 2014

### PROJECT KICKOFF

November 22, 2013

-----  
**May 28th through June 10th, 2014**

#### CELLAR:

Install 6" piping in print room.

#### ENTRY:

Cut pipe riser openings.  
Insulate new ductwork and close ceiling.

#### 2nd FLOOR:

Relocate electrical ductwork points.  
Finish ductwork in corridor.

#### 3rd FLOOR:

Electrical rough ins continue north and south.

#### 5th FLOOR:

Demolish & reinstall new sprinkler piping south side-24/7 Fireguard  
Electrical rough ins continue north and south.  
Install ductwork north and south.  
Wall framing north and south continues.

#### 6th FLOOR:


Duct survey.  
Install steel in shaft.  
Airflow testing.

#### ROOF:

Demolish EIFS wall.  
Cut roof opening and cover.



LiRO Construction Management on 5th Floor

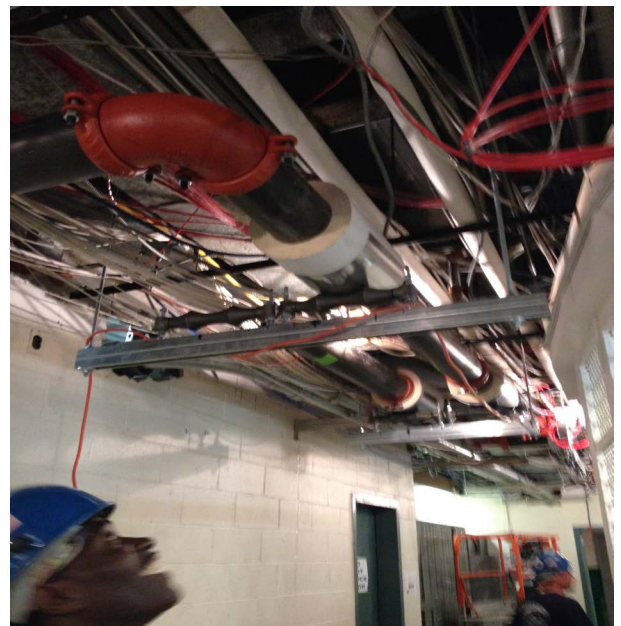

Cellar level corridor.

## Space Planning & Capital Projects

### Backfill Construction Update June 15, 2014

#### June 11th through 24th, 2014

##### CELLAR:

- Dance studio piping.
- Insulate pipe- green & dressing rooms.
- Firestop openings.
- Sprinkler demo and reinstallation.

##### BASEMENT:

- Fire hose cabinet reloaction.
- Install pipe opening and steel at pit.

##### ENTRY:

- Cut pipe riser openings.
- Insulate new ductwork and close ceiling.

##### 2nd FLOOR:

- Sprinkler pipe relocation.
- Reloacte drain line and risers in MER.

##### 3rd FLOOR:

- Electrical rough ins continue north and south.
- Relocate sprinkler heads @ pipe shaft.
- Install ductwork.

##### 5th FLOOR:

- Install branch lines and sprinkler heads north & south side-24/7 Fireguard
- Electrical rough ins continue north and south.
- Continue ductwork north and south.
- Fire hose cabinet relocation.
- Sheetrock delivery through window.

##### ROOF:

- CMU curb installation around opening.



Cellar level piping installed through stock room



Roof penetration where new MAU will be housed.



New sprinkler lines- 5th floor.
